

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
1	Granbury ISD Phase I	8.15	175 d	Wed 3/19/14	Tue 11/18/14	0%			
2	Recieve 100% Drawings	0 d	Wed 3/19/14	Wed 3/19/14	100%	◆ 3/19			
3	Bid Day	0 d	Tue 4/22/14	Tue 4/22/14	0%		◆ 4/22		
4	Board Meeting	0 d	Mon 5/12/14	Mon 5/12/14	0%			◆ 5/12	
5	Start Construction	0 d	Mon 5/26/14	Mon 5/26/14	0%				◆ 5/26
6	Materials & Submittals - Acquisition	36 d	Mon 5/26/14	Mon 7/14/14	0%				
7	Project 'C' - Emma Roberson Elementary (Renovations)	50 d	Wed 6/11/14	Tue 8/19/14	0%				
8	Demolition Of Interior Remodel Area	4 d	Wed 6/11/14	Mon 6/16/14	0%				
9	Security Vestibules - R & R Storefront & Doors	2 d	Wed 6/11/14	Thu 6/12/14	0%				
10	MEP - OH Rough in	10 d	Tue 6/17/14	Mon 6/30/14	0%				
11	Hollow Metal Frames - Delivery	1 d	Tue 6/17/14	Tue 6/17/14	0%				
12	Security Vestibules - Electrical Rough-In	5 d	Thu 6/19/14	Wed 6/25/14	0%				
13	Drywall - Frame Interior Walls	4 d	Thu 6/19/14	Tue 6/24/14	0%				
14	MEP - Wall Rough-In	6 d	Fri 6/20/14	Fri 6/27/14	0%				
15	Storefronts, Glass & Glazing	4 d	Wed 6/25/14	Mon 6/30/14	0%				
16	Drywall - Sheetrock Walls First Side	4 d	Mon 6/23/14	Thu 6/26/14	0%				
17	Roofing - Repair @ RTU's	3 d	Tue 7/1/14	Thu 7/3/14	0%				
18	Fire Alarm	4 d	Tue 7/1/14	Fri 7/4/14	0%				
19	Drywall - Sheetrock Walls Second Side	4 d	Fri 6/27/14	Wed 7/2/14	0%				
20	T, B, T, & Paint	12 d	Mon 6/30/14	Tue 7/15/14	0%				
21	Security Vestibules - Patch, Repair & Paint As Needed	4 d	Mon 6/30/14	Thu 7/3/14	0%				
22	Security Vestibules - Install Devices	4 d	Fri 7/4/14	Wed 7/9/14	0%				
23	Ceramic Tile	10 d	Mon 7/7/14	Fri 7/18/14	0%				
24	MEP - Wall & OH Trim Out	10 d	Thu 7/10/14	Wed 7/23/14	0%				
25	Flooring -	4 d	Wed 7/16/14	Mon 7/21/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
26	Plumbing - Set Fixtures	10 d	Fri 7/18/14	Thu 7/31/14	0%				
27	Doors & Hardware	2 d	Tue 7/22/14	Wed 7/23/14	0%				
28	Signage - Interior	2 d	Tue 7/22/14	Wed 7/23/14	0%				
29	MEP - Startup Equipment	2 d	Thu 7/24/14	Fri 7/25/14	0%				
30	Test & Balance HVAC Systems	5 d	Mon 7/28/14	Fri 8/1/14	0%				
31	Final Clean	8 d	Tue 8/5/14	Thu 8/14/14	0%				
32	Punch List	3 d	Fri 8/15/14	Tue 8/19/14	0%				
33	Project 'E' - Oakwoods Elementary School (Addition)	127 d	Mon 5/26/14	Tue 11/18/14	0%				
34	Structural - Steel, Joist & Decking Submittals	30 d	Mon 5/26/14	Fri 7/4/14	0%				
35	Selective Site Demolitions	6 d	Mon 6/16/14	Mon 6/23/14	0%				
36	Excavation - Cut & Fill	4 d	Tue 6/24/14	Fri 6/27/14	0%				
37	Concrete - Drilled Piers 16	4 d	Mon 6/30/14	Thu 7/3/14	0%				
38	Concrete - Grade Beams	5 d	Fri 7/4/14	Thu 7/10/14	0%				
39	Plumbing - Under Floor Rough-In	4 d	Fri 7/11/14	Wed 7/16/14	0%				
40	Concrete - Slab On Void Boxes	8 d	Thu 7/17/14	Mon 7/28/14	0%				
41	Hollow Metal Frames - Delivery	1 d	Tue 7/29/14	Tue 7/29/14	0%				
42	Masonry - Exterior CMU Walls	14 d	Thu 7/31/14	Tue 8/19/14	0%				
43	MEP - Wall Rough in	25 d	Fri 8/1/14	Thu 9/4/14	0%				
44	Structural - Steel, Joist & Decking Fab & Delivery	15 d	Mon 7/28/14	Fri 8/15/14	0%				
45	Masonry - Exterior Veneer	10 d	Wed 8/20/14	Tue 9/2/14	0%				
46	Structural Cols, Beam - Erection	3 d	Wed 8/27/14	Fri 8/29/14	0%				
47	Structural - Joists & Decking Erection	5 d	Mon 9/1/14	Fri 9/5/14	0%				
48	Drywall - Frame Interior Walls	8 d	Wed 9/3/14	Fri 9/12/14	0%				
49	Roofing - B U Roofing	8 d	Mon 9/8/14	Wed 9/17/14	0%				
50	MEP - OH Rough in	10 d	Wed 9/10/14	Tue 9/23/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
51	Storefronts, Glass & Glazing	4 d	Mon 9/15/14	Thu 9/18/14	0%				
52	Drywall - Sheetrock Walls First Side	4 d	Mon 9/15/14	Thu 9/18/14	0%				
53	Drywall - Sheetrock Walls Second Side	5 d	Tue 9/16/14	Mon 9/22/14	0%				
54	Set RTU's	2 d	Thu 9/18/14	Fri 9/19/14	0%				
55	Pre-Manufactured Aluminum Canopy	8 d	Thu 9/18/14	Mon 9/29/14	0%				
56	Concrete - Walks & Flatwork	10 d	Thu 9/18/14	Wed 10/1/14	0%				
57	Roofing - Metal Trim	4 d	Thu 9/18/14	Tue 9/23/14	0%				
58	Fencing	5 d	Tue 9/23/14	Mon 9/29/14	0%				
59	Block-Fill, T, B, T, & Paint	12 d	Tue 9/23/14	Wed 10/8/14	0%				
60	Fire Alarm	4 d	Wed 9/24/14	Mon 9/29/14	0%				
61	Signage - Interior & Exterior	2 d	Tue 9/30/14	Wed 10/1/14	0%				
62	Landscaping & Irrigation	12 d	Thu 10/2/14	Fri 10/17/14	0%				
63	Parking Striping & Signs	2 d	Thu 10/2/14	Fri 10/3/14	0%				
64	Ceramic Tile	10 d	Wed 10/1/14	Tue 10/14/14	0%				
65	Ceiling - Suspended Grid	4 d	Thu 10/9/14	Tue 10/14/14	0%				
66	MEP - Wall & OH Trim Out	10 d	Fri 10/10/14	Thu 10/23/14	0%				
67	Plumbing - Set Fixtures	10 d	Tue 10/14/14	Mon 10/27/14	0%				
68	Ceiling - Drop Tiles	4 d	Wed 10/22/14	Mon 10/27/14	0%				
69	Flooring -	6 d	Thu 10/23/14	Thu 10/30/14	0%				
70	MEP - Startup Equipment	2 d	Tue 10/28/14	Wed 10/29/14	0%				
71	Doors & Hardware	3 d	Thu 10/30/14	Mon 11/3/14	0%				
72	Test & Balance HVAC Systems	5 d	Tue 11/4/14	Mon 11/10/14	0%				
73	Final Clean	2 d	Wed 11/12/14	Thu 11/13/14	0%				
74	Punch List	3 d	Fri 11/14/14	Tue 11/18/14	0%				
75	Project 'E' - Oakwoods Elementary School (Renovations)	50 d	Wed 6/11/14	Tue 8/19/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
76	Demolition Of Interior Remodel Area	4 d	Wed 6/11/14	Mon 6/16/14	0%				
77	Security Vestibules - R & R Storefront & Doors	2 d	Wed 6/11/14	Thu 6/12/14	0%				
78	MEP - OH Rough in	10 d	Tue 6/17/14	Mon 6/30/14	0%				
79	Security Vestibules - Electrical Rough-In	5 d	Wed 6/18/14	Tue 6/24/14	0%				
80	Drywall - Frame Interior Walls	4 d	Wed 6/18/14	Mon 6/23/14	0%				
81	MEP - Wall Rough-In	10 d	Wed 6/18/14	Tue 7/1/14	0%				
82	Drywall - Sheetrock Walls First Side	4 d	Fri 6/20/14	Wed 6/25/14	0%				
83	Roofing - Repair @ RTU's	3 d	Wed 7/2/14	Fri 7/4/14	0%				
84	Fire Alarm	4 d	Tue 7/1/14	Fri 7/4/14	0%				
85	Drywall - Sheetrock Walls Second Side	5 d	Thu 6/26/14	Wed 7/2/14	0%				
86	T, B, T, & Paint	12 d	Thu 6/26/14	Fri 7/11/14	0%				
87	Security Vestibules - Patch, Repair & Paint As Needed	4 d	Thu 6/26/14	Tue 7/1/14	0%				
88	Set RTU's	2 d	Mon 7/7/14	Tue 7/8/14	0%				
89	Concrete - Walks & Flatwork	10 d	Mon 7/7/14	Fri 7/18/14	0%				
90	Security Vestibules - Install Devices	4 d	Wed 7/2/14	Mon 7/7/14	0%				
91	Storefronts, Glass & Glazing	4 d	Thu 7/3/14	Tue 7/8/14	0%				
92	Ceramic Tile	10 d	Mon 7/7/14	Fri 7/18/14	0%				
93	Flooring -	6 d	Mon 7/14/14	Mon 7/21/14	0%				
94	Ceiling - Suspended Grid	4 d	Tue 7/15/14	Fri 7/18/14	0%				
95	Plumbing - Set Fixtures	8 d	Thu 7/17/14	Mon 7/28/14	0%				
96	MEP - Wall & OH Trim Out	10 d	Mon 7/21/14	Fri 8/1/14	0%				
97	Doors & Hardware	2 d	Tue 7/22/14	Wed 7/23/14	0%				
98	Signage - Interior	2 d	Thu 7/24/14	Fri 7/25/14	0%				
99	Ceiling - Drop Tiles	3 d	Mon 8/4/14	Wed 8/6/14	0%				
100	MEP - Startup Equipment	2 d	Mon 8/4/14	Tue 8/5/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
101	Test & Balance HVAC Systems	5 d	Wed 8/6/14	Tue 8/12/14	0%				
102	Final Clean	2 d	Wed 8/13/14	Thu 8/14/14	0%				
103	Punch List	3 d	Fri 8/15/14	Tue 8/19/14	0%				
104	Project 'G' - Acton Middle School (Renovations)	43 d	Mon 6/16/14	Wed 8/13/14	0%				
105	Dust Control & Barriers	2 d	Mon 6/16/14	Tue 6/17/14	0%				
106	Electrical - Make Safe For Demolition	2 d	Mon 6/16/14	Tue 6/17/14	0%				
107	Selective Demolitions	5 d	Mon 6/16/14	Fri 6/20/14	0%				
108	Hollow Metal Frames - Delivery	1 d	Wed 6/18/14	Wed 6/18/14	0%				
109	Drywall - Framing Interior Walls	10 d	Thu 6/19/14	Wed 7/2/14	0%				
110	Masonry - Interior CMU & Brick Veneer	7 d	Mon 6/23/14	Tue 7/1/14	0%				
111	Steel Bent Plate Lintel	1 d	Mon 6/23/14	Mon 6/23/14	0%				
112	Plumbing - Reroute Supply Water Line	5 d	Mon 6/23/14	Fri 6/27/14	0%				
113	MEP - OH Rough in	8 d	Mon 6/23/14	Wed 7/2/14	0%				
114	MEP - Wall Rough in	15 d	Mon 6/23/14	Fri 7/11/14	0%				
115	Fire Sprinkler - OH Rough in	3 d	Tue 7/1/14	Thu 7/3/14	0%				
116	Roofing - B U Roofing	8 d	Thu 7/3/14	Mon 7/14/14	0%				
117	Sheetrock - First Side	3 d	Thu 7/3/14	Mon 7/7/14	0%				
118	T, B, T, & Paint	10 d	Mon 7/7/14	Fri 7/18/14	0%				
119	Sheetrock - Second Side	3 d	Tue 7/8/14	Thu 7/10/14	0%				
120	Demo/Patch Existing Terrazzo	7 d	Fri 7/11/14	Mon 7/21/14	0%				
121	Security Vestibules - Aluminum Storefront Doors	4 d	Fri 7/11/14	Wed 7/16/14	0%				
122	Ceramic Tile	8 d	Fri 7/11/14	Tue 7/22/14	0%				
123	Security Vestibules - Electrical Rough-In	5 d	Mon 7/14/14	Fri 7/18/14	0%				
124	Millwork	5 d	Tue 7/15/14	Mon 7/21/14	0%				
125	Flooring - VCT & Carpet	8 d	Tue 7/15/14	Thu 7/24/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
126	Ceiling - Suspended Grid	3 d	Fri 7/18/14	Tue 7/22/14	0%				
127	MEP - Wall & OH Trim Out	5 d	Fri 7/18/14	Thu 7/24/14	0%				
128	Doors & Hardware	3 d	Fri 7/18/14	Tue 7/22/14	0%				
129	Security Vestibules - Install Devices	6 d	Mon 7/21/14	Mon 7/28/14	0%				
130	MEP - Startup Equipment	3 d	Tue 7/22/14	Thu 7/24/14	0%				
131	Fire Alarm	5 d	Wed 7/23/14	Tue 7/29/14	0%				
132	Ceiling - Drop Tiles	3 d	Tue 7/29/14	Thu 7/31/14	0%				
133	Test & Balance HVAC Systems	2 d	Fri 8/1/14	Mon 8/4/14	0%				
134	Misc. Specialties - MB, TB, FEC, PS, HB	4 d	Fri 8/1/14	Wed 8/6/14	0%				
135	Final Clean	2 d	Thu 8/7/14	Fri 8/8/14	0%				
136	Punch List	3 d	Mon 8/11/14	Wed 8/13/14	0%				
137	Project 'H' - Granbury Middle School (Renovations)	43 d	Mon 6/16/14	Wed 8/13/14	0%				
138	Dust Control & Barriers	2 d	Mon 6/16/14	Tue 6/17/14	0%				
139	Electrical - Make Safe For Demolition	2 d	Mon 6/16/14	Tue 6/17/14	0%				
140	Selective Demolitions	5 d	Wed 6/18/14	Tue 6/24/14	0%				
141	Hollow Metal Frames - Delivery	1 d	Fri 6/20/14	Fri 6/20/14	0%				
142	Steel Bent Plate Lintel	1 d	Wed 6/25/14	Wed 6/25/14	0%				
143	Masonry - Interior CMU & Brick Veneer	7 d	Wed 6/25/14	Thu 7/3/14	0%				
144	Plumbing - Reroute Water Supply Line	5 d	Wed 6/25/14	Tue 7/1/14	0%				
145	MEP - OH Rough in	8 d	Wed 6/25/14	Fri 7/4/14	0%				
146	MEP - Wall Rough in	15 d	Wed 6/25/14	Tue 7/15/14	0%				
147	Drywall - Framing Interior Walls	10 d	Fri 6/27/14	Thu 7/10/14	0%				
148	Fire Sprinkler - OH Rough in	3 d	Thu 7/3/14	Mon 7/7/14	0%				
149	Roofing - B U Roofing	8 d	Mon 7/7/14	Wed 7/16/14	0%				
150	Sheetrock - First Side	3 d	Fri 7/11/14	Tue 7/15/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
151	Security Vestibules - Electrical Rough-In	5 d	Wed 7/16/14	Tue 7/22/14	0%				
152	Sheetrock - Second Side	3 d	Wed 7/16/14	Fri 7/18/14	0%				
153	T, B, T, & Paint	10 d	Wed 7/16/14	Tue 7/29/14	0%				
154	Demo/Patch Existing Terrazzo	7 d	Mon 7/21/14	Tue 7/29/14	0%				
155	Security Vestibules - Aluminum Storefront Doors	4 d	Mon 7/21/14	Thu 7/24/14	0%				
156	Ceramic Tile	8 d	Tue 7/22/14	Thu 7/31/14	0%				
157	Millwork	5 d	Thu 7/24/14	Wed 7/30/14	0%				
158	Ceiling - Suspended Grid	3 d	Fri 7/25/14	Tue 7/29/14	0%				
159	MEP - Wall & OH Trim Out	5 d	Fri 7/25/14	Thu 7/31/14	0%				
160	Flooring - VCT & Carpet	8 d	Mon 7/28/14	Wed 8/6/14	0%				
161	Fire Alarm	5 d	Wed 7/30/14	Tue 8/5/14	0%				
162	Security Vestibules - Install Devices	6 d	Wed 7/30/14	Wed 8/6/14	0%				
163	MEP - Startup Equipment	3 d	Fri 8/1/14	Tue 8/5/14	0%				
164	Ceiling - Drop Tiles	3 d	Fri 8/1/14	Tue 8/5/14	0%				
165	Misc. Specialties - MB, TB, FEC, PS, HB	4 d	Fri 8/1/14	Wed 8/6/14	0%				
166	Doors & Hardware	2 d	Tue 8/5/14	Wed 8/6/14	0%				
167	Test & Balance HVAC Systems	2 d	Tue 8/5/14	Wed 8/6/14	0%				
168	Final Clean	2 d	Thu 8/7/14	Fri 8/8/14	0%				
169	Punch List	3 d	Mon 8/11/14	Wed 8/13/14	0%				
170	Project 'B' - Baccus Elementary School (Renovations)	58 d	Tue 6/3/14	Thu 8/21/14	0%				
171	Dust Control & Barriers	2 d	Tue 6/3/14	Wed 6/4/14	0%				
172	Electrical - Make Safe For Demolition	2 d	Tue 6/3/14	Wed 6/4/14	0%				
173	Selective Demolitions	5 d	Fri 6/20/14	Thu 6/26/14	0%				
174	Hollow Metal Frames - Delivery	1 d	Tue 6/24/14	Tue 6/24/14	0%				
175	Plumbing - Under Floor Rough-In	7 d	Fri 6/27/14	Mon 7/7/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
176	Drywall - Framing Interior Walls & Hard Ceilings	5 d	Fri 6/27/14	Thu 7/3/14	0%				
177	MEP - OH Rough in	10 d	Fri 6/27/14	Thu 7/10/14	0%				
178	Roofing - Demo & Patch @ RTU Curbs	5 d	Fri 6/27/14	Thu 7/3/14	0%				
179	MEP - Wall Rough in	5 d	Mon 6/30/14	Fri 7/4/14	0%				
180	Sheetrock - First Side	6 d	Fri 7/4/14	Fri 7/11/14	0%				
181	Fire Sprinkler - OH Rough in	6 d	Mon 7/7/14	Mon 7/14/14	0%				
182	Security Vestibules - Electrical Rough-In	5 d	Mon 7/7/14	Fri 7/11/14	0%				
183	HVAC - Set Equipment	3 d	Fri 7/11/14	Tue 7/15/14	0%				
184	Sheetrock - Second Side & Hard Ceilings	6 d	Mon 7/14/14	Mon 7/21/14	0%				
185	T, B, T, & Paint	10 d	Mon 7/14/14	Fri 7/25/14	0%				
186	Ceramic Tile	8 d	Fri 7/18/14	Tue 7/29/14	0%				
187	Security Vestibules - Install Storefront Doors	3 d	Tue 7/22/14	Thu 7/24/14	0%				
188	Millwork	10 d	Tue 7/22/14	Mon 8/4/14	0%				
189	Ceiling - Suspended Grid	6 d	Thu 7/24/14	Thu 7/31/14	0%				
190	MEP - Wall & OH Trim Out	10 d	Thu 7/24/14	Wed 8/6/14	0%				
191	Plumbing - Set Fixtures	10 d	Fri 7/25/14	Thu 8/7/14	0%				
192	Flooring - VCT & Carpet	8 d	Tue 7/29/14	Thu 8/7/14	0%				
193	Fire Alarm	5 d	Fri 8/1/14	Thu 8/7/14	0%				
194	Doors & Hardware	3 d	Fri 8/1/14	Tue 8/5/14	0%				
195	Reinstall Lockers	3 d	Fri 8/1/14	Tue 8/5/14	0%				
196	Security Vestibules - Install Devices	4 d	Mon 8/4/14	Thu 8/7/14	0%				
197	Toilet Partitions & Accessories	3 d	Wed 8/6/14	Fri 8/8/14	0%				
198	MEP - Startup Equipment	3 d	Thu 8/7/14	Mon 8/11/14	0%				
199	Ceiling - Drop Tiles	3 d	Thu 8/7/14	Mon 8/11/14	0%				
200	Misc. Specialties - MB, TB, FEC, PS, HB	4 d	Thu 8/7/14	Tue 8/12/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
201	Test & Balance HVAC Systems	4 d	Fri 8/8/14	Wed 8/13/14	0%				
202	Final Clean	2 d	Thu 8/14/14	Fri 8/15/14	0%				
203	Punch List	4 d	Mon 8/18/14	Thu 8/21/14	0%				
204	Project 'D' - Mambrino Elementary School (Renovations)	46 d	Wed 6/18/14	Wed 8/20/14	0%				
205	Dust Control & Barriers	2 d	Wed 6/18/14	Thu 6/19/14	0%				
206	Electrical - Make Safe For Demolition	2 d	Wed 6/18/14	Thu 6/19/14	0%				
207	Selective Demolitions	5 d	Fri 6/20/14	Thu 6/26/14	0%				
208	Hollow Metal Frames - Delivery	1 d	Tue 6/24/14	Tue 6/24/14	0%				
209	Drywall - Framing Interior Walls	5 d	Wed 6/25/14	Tue 7/1/14	0%				
210	MEP - OH Rough in	6 d	Wed 6/25/14	Wed 7/2/14	0%				
211	Roofing - Demo & Patch @ RTU Curbs	5 d	Wed 6/25/14	Tue 7/1/14	0%				
212	MEP - Wall Rough in	5 d	Thu 6/26/14	Wed 7/2/14	0%				
213	HVAC - Set Equipment	3 d	Mon 6/30/14	Wed 7/2/14	0%				
214	Sheetrock - First Side	3 d	Wed 7/2/14	Fri 7/4/14	0%				
215	Fire Sprinkler - OH Rough in	3 d	Thu 7/3/14	Mon 7/7/14	0%				
216	Security Vestibules - Electrical Rough-In	5 d	Thu 7/3/14	Wed 7/9/14	0%				
217	Sheetrock - Second Side	3 d	Mon 7/7/14	Wed 7/9/14	0%				
218	T, B, T, & Paint	10 d	Tue 7/8/14	Mon 7/21/14	0%				
219	Security Vestibules - Install Storefront Doors	4 d	Thu 7/10/14	Tue 7/15/14	0%				
220	Ceramic Tile	8 d	Mon 7/14/14	Wed 7/23/14	0%				
221	Millwork	10 d	Thu 7/17/14	Wed 7/30/14	0%				
222	Ceiling - Suspended Grid	3 d	Tue 7/22/14	Thu 7/24/14	0%				
223	MEP - Wall & OH Trim Out	5 d	Tue 7/22/14	Mon 7/28/14	0%				
224	Fire Alarm	5 d	Fri 7/25/14	Thu 7/31/14	0%				
225	Flooring - VCT & Carpet	6 d	Mon 7/28/14	Mon 8/4/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
226	MEP - Startup Equipment	3 d	Tue 7/29/14	Thu 7/31/14	0%				
227	Ceiling - Drop Tiles	3 d	Tue 7/29/14	Thu 7/31/14	0%				
228	Security Vestibules - Install Devices	4 d	Tue 7/29/14	Fri 8/1/14	0%				
229	Misc. Specialties - MB, TB, FEC, PS, HB	4 d	Fri 8/1/14	Wed 8/6/14	0%				
230	Doors & Hardware	3 d	Tue 8/5/14	Thu 8/7/14	0%				
231	Test & Balance HVAC Systems	3 d	Fri 8/8/14	Tue 8/12/14	0%				
232	Final Clean	2 d	Wed 8/13/14	Thu 8/14/14	0%				
233	Punch List	4 d	Fri 8/15/14	Wed 8/20/14	0%				
234	Project 'A' - Acton Elementary School (Renovations)	38 d	Mon 6/30/14	Wed 8/20/14	0%				
235	Demolition Of Interior Remodel Area	3 d	Mon 6/30/14	Wed 7/2/14	0%				
236	Security Vestibules - R & R Storefront & Doors	2 d	Tue 7/1/14	Wed 7/2/14	0%				
237	MEP - OH Rough in	10 d	Tue 7/1/14	Mon 7/14/14	0%				
238	Drywall - Frame Interior Walls	3 d	Thu 7/3/14	Mon 7/7/14	0%				
239	Storefronts, Glass & Glazing	4 d	Thu 7/3/14	Tue 7/8/14	0%				
240	MEP - Wall Rough-In	6 d	Thu 7/3/14	Thu 7/10/14	0%				
241	Security Vestibules - Frame Hard Ceiling	3 d	Mon 7/7/14	Wed 7/9/14	0%				
242	Security Vestibules - Electrical Rough-In	4 d	Tue 7/8/14	Fri 7/11/14	0%				
243	Drywall - Sheetrock Walls First Side	3 d	Tue 7/8/14	Thu 7/10/14	0%				
244	Roofing - Repair @ RTU's	3 d	Tue 7/15/14	Thu 7/17/14	0%				
245	Fire Alarm	4 d	Tue 7/15/14	Fri 7/18/14	0%				
246	Drywall - Sheetrock Walls Second Side	3 d	Fri 7/11/14	Tue 7/15/14	0%				
247	Security Vestibules - Sheetrock Hard Ceiling	2 d	Mon 7/14/14	Tue 7/15/14	0%				
248	Security Vestibules - Patch, Repair & Paint As Needed	4 d	Wed 7/16/14	Mon 7/21/14	0%				
249	T, B, T, & Paint	8 d	Wed 7/16/14	Fri 7/25/14	0%				
250	Security Vestibules - Install Devices	4 d	Tue 7/22/14	Fri 7/25/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
251	Ceramic Tile	5 d	Wed 7/23/14	Tue 7/29/14	0%				
252	Flooring -	5 d	Mon 7/28/14	Fri 8/1/14	0%				
253	MEP - Wall & OH Trim Out	8 d	Wed 7/30/14	Fri 8/8/14	0%				
254	Plumbing - Set Fixtures	10 d	Wed 7/30/14	Tue 8/12/14	0%				
255	Doors & Hardware	2 d	Mon 8/4/14	Tue 8/5/14	0%				
256	Signage - Interior	2 d	Mon 8/4/14	Tue 8/5/14	0%				
257	Toilet Accessories	3 d	Fri 8/8/14	Tue 8/12/14	0%				
258	MEP - Startup Equipment	2 d	Mon 8/11/14	Tue 8/12/14	0%				
259	Test & Balance HVAC Systems	2 d	Wed 8/13/14	Thu 8/14/14	0%				
260	Final Clean	2 d	Fri 8/15/14	Mon 8/18/14	0%				
261	Punch List	2 d	Tue 8/19/14	Wed 8/20/14	0%				
262	Project 'F' - Brawner Intermediate School (Renovations)	48 d	Tue 6/3/14	Thu 8/7/14	0%				
263	Dust Control & Barriers	2 d	Tue 6/3/14	Wed 6/4/14	0%				
264	Electrical - Make Safe For Demolition	2 d	Thu 6/26/14	Fri 6/27/14	0%				
265	Selective Demolitions	5 d	Mon 6/30/14	Fri 7/4/14	0%				
266	Hollow Metal Frames - Delivery	1 d	Wed 7/2/14	Wed 7/2/14	0%				
267	Drywall - Framing Interior Walls	5 d	Mon 7/7/14	Fri 7/11/14	0%				
268	MEP - OH Rough in	6 d	Mon 7/7/14	Mon 7/14/14	0%				
269	MEP - Wall Rough in	5 d	Tue 7/8/14	Mon 7/14/14	0%				
270	Sheetrock - First Side	3 d	Fri 7/11/14	Tue 7/15/14	0%				
271	Fire Sprinkler - OH Rough in	3 d	Tue 7/15/14	Thu 7/17/14	0%				
272	Security Vestibules - Electrical Rough-In	5 d	Tue 7/15/14	Mon 7/21/14	0%				
273	Sheetrock - Second Side	3 d	Wed 7/16/14	Fri 7/18/14	0%				
274	T, B, T, & Paint	5 d	Wed 7/16/14	Tue 7/22/14	0%				
275	Ceramic Tile	5 d	Wed 7/16/14	Tue 7/22/14	0%				

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

ID	Task Name	Duration	Start	Finish	% Complete	March	April	May	June
276	Millwork	5 d	Thu 7/17/14	Wed 7/23/14	0%				
277	Security Vestibules - Aluminum Storefront Doors	3 d	Mon 7/21/14	Wed 7/23/14	0%				
278	Ceiling - Suspended Grid	3 d	Mon 7/21/14	Wed 7/23/14	0%				
279	MEP - Wall & OH Trim Out	5 d	Mon 7/21/14	Fri 7/25/14	0%				
280	Doors & Hardware	2 d	Mon 7/21/14	Tue 7/22/14	0%				
281	Flooring - VCT & Carpet	4 d	Tue 7/22/14	Fri 7/25/14	0%				
282	Fire Alarm	5 d	Thu 7/24/14	Wed 7/30/14	0%				
283	MEP - Startup Equipment	2 d	Mon 7/28/14	Tue 7/29/14	0%				
284	Ceiling - Drop Tiles	3 d	Mon 7/28/14	Wed 7/30/14	0%				
285	Misc. Specialties - MB, TB, FEC, PS, HB	4 d	Mon 7/28/14	Thu 7/31/14	0%				
286	Test & Balance HVAC Systems	2 d	Tue 7/29/14	Wed 7/30/14	0%				
287	Security Vestibules - Install Devices	6 d	Wed 7/30/14	Wed 8/6/14	0%				
288	Final Clean	2 d	Fri 8/1/14	Mon 8/4/14	0%				
289	Punch List	3 d	Tue 8/5/14	Thu 8/7/14	0%				

Granbury ISD Renovations 2014




Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

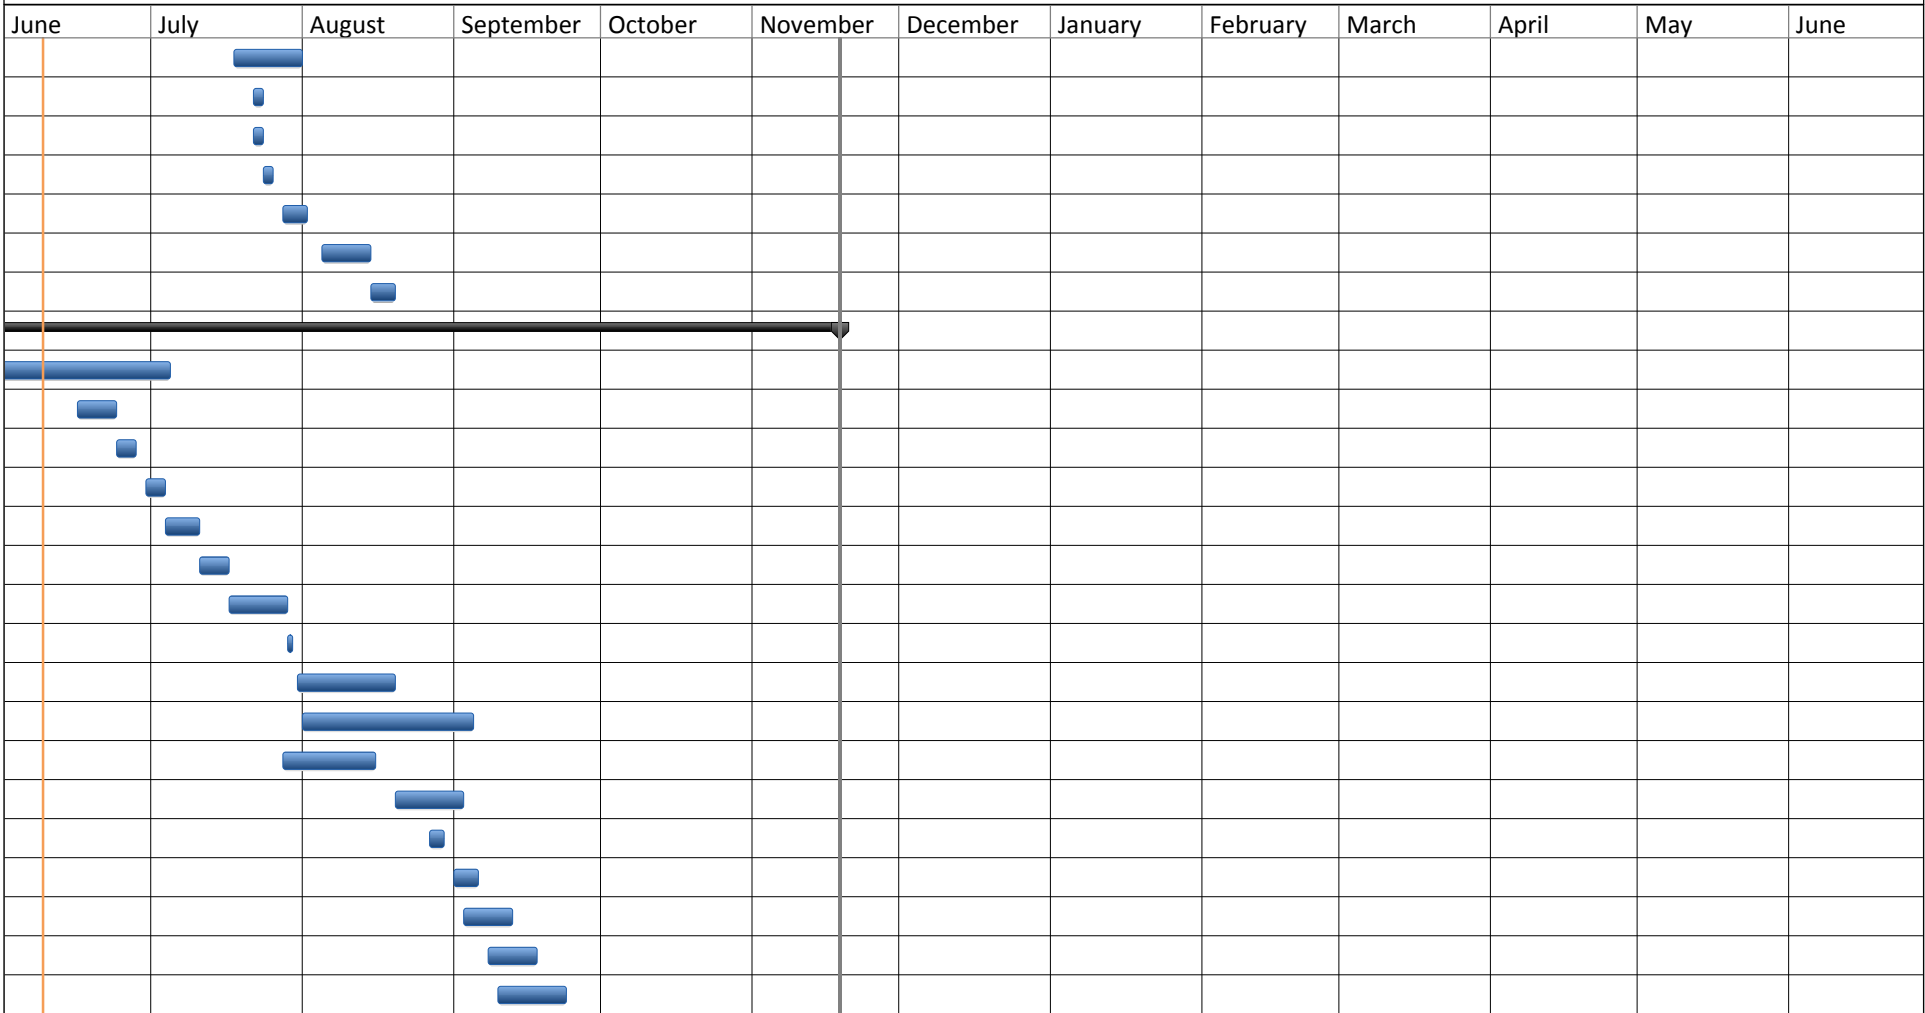

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014



Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014




Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

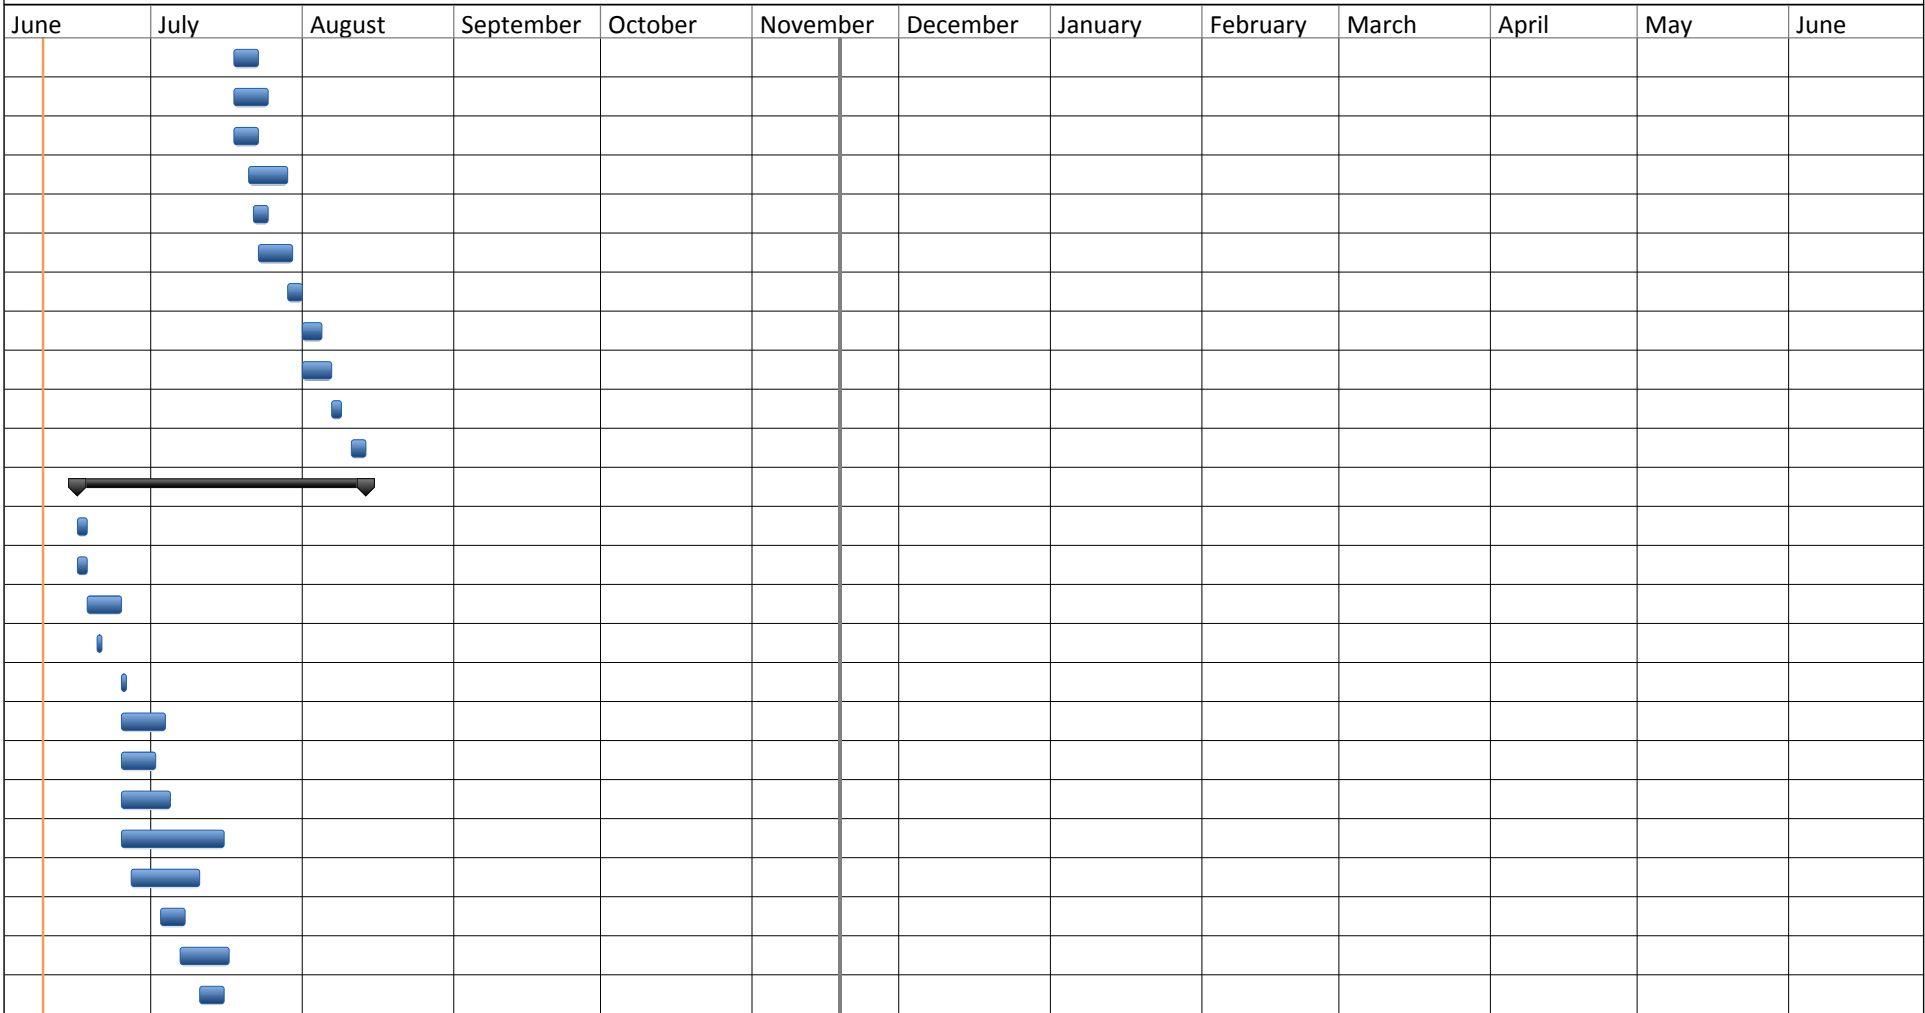

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014



Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014




Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

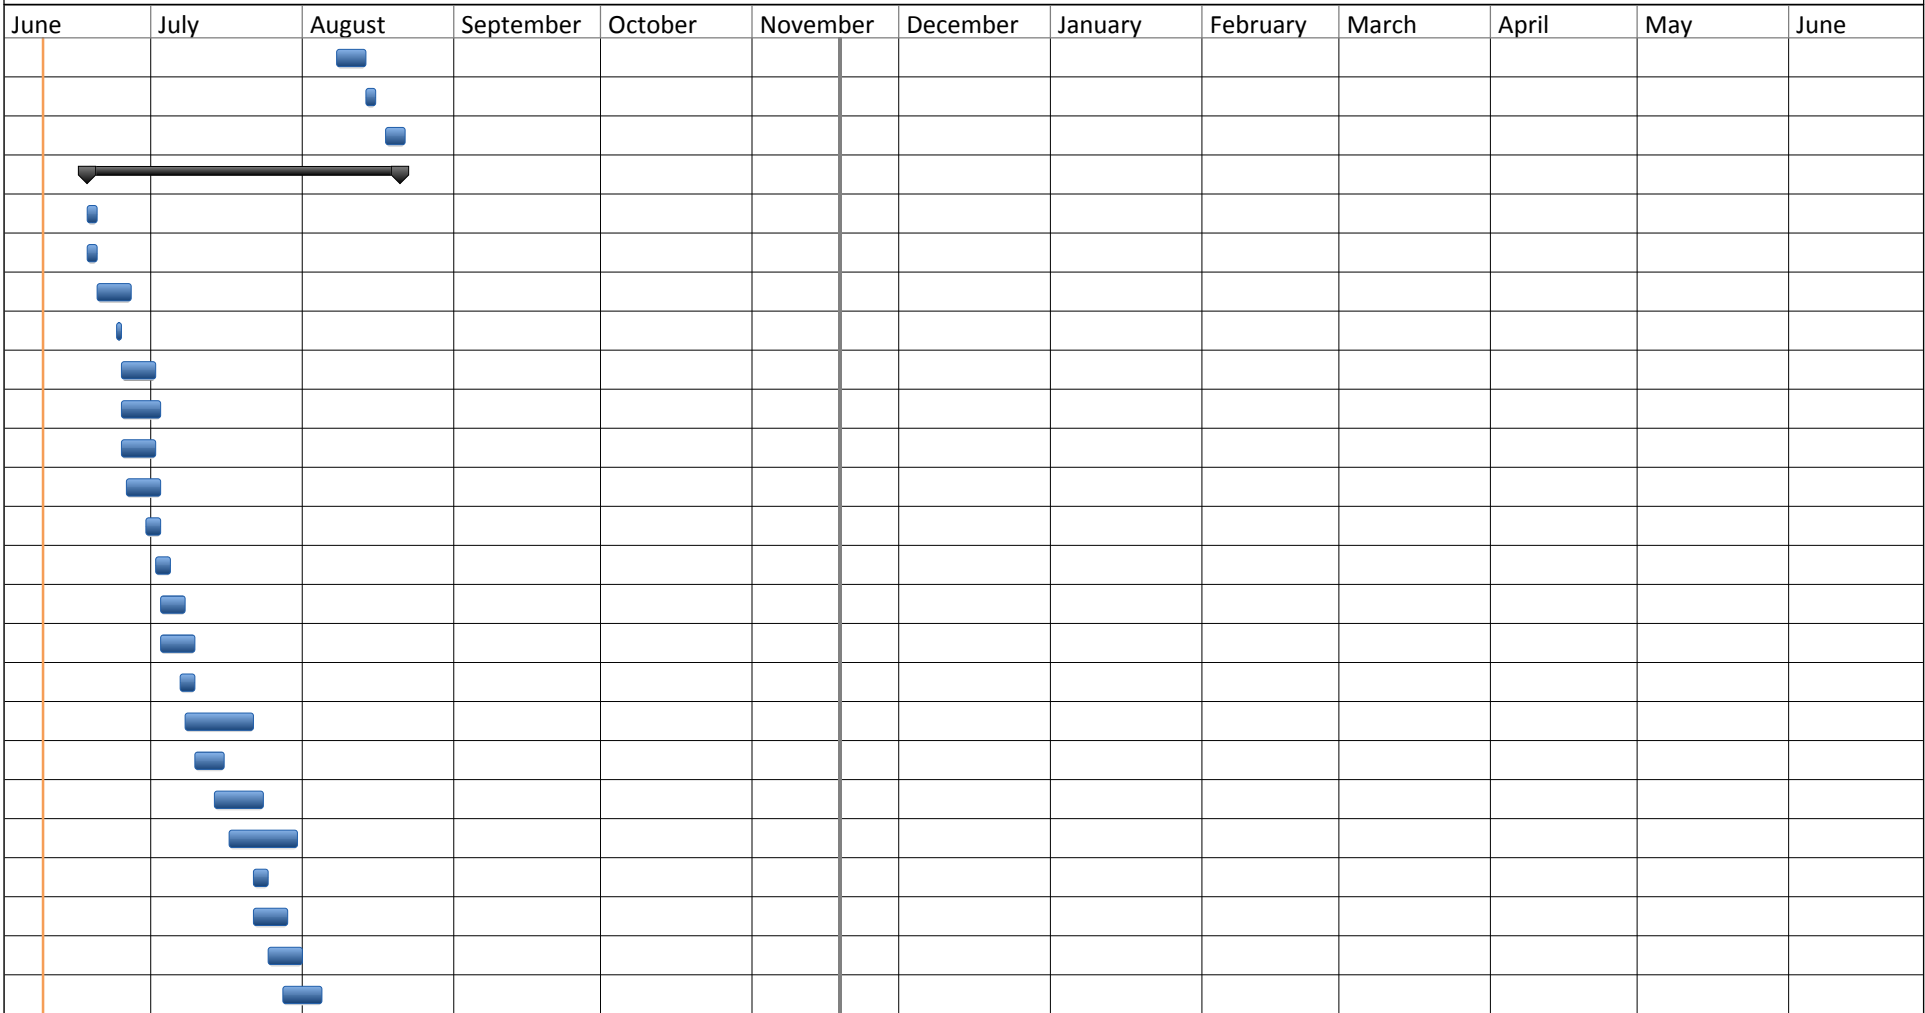


Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

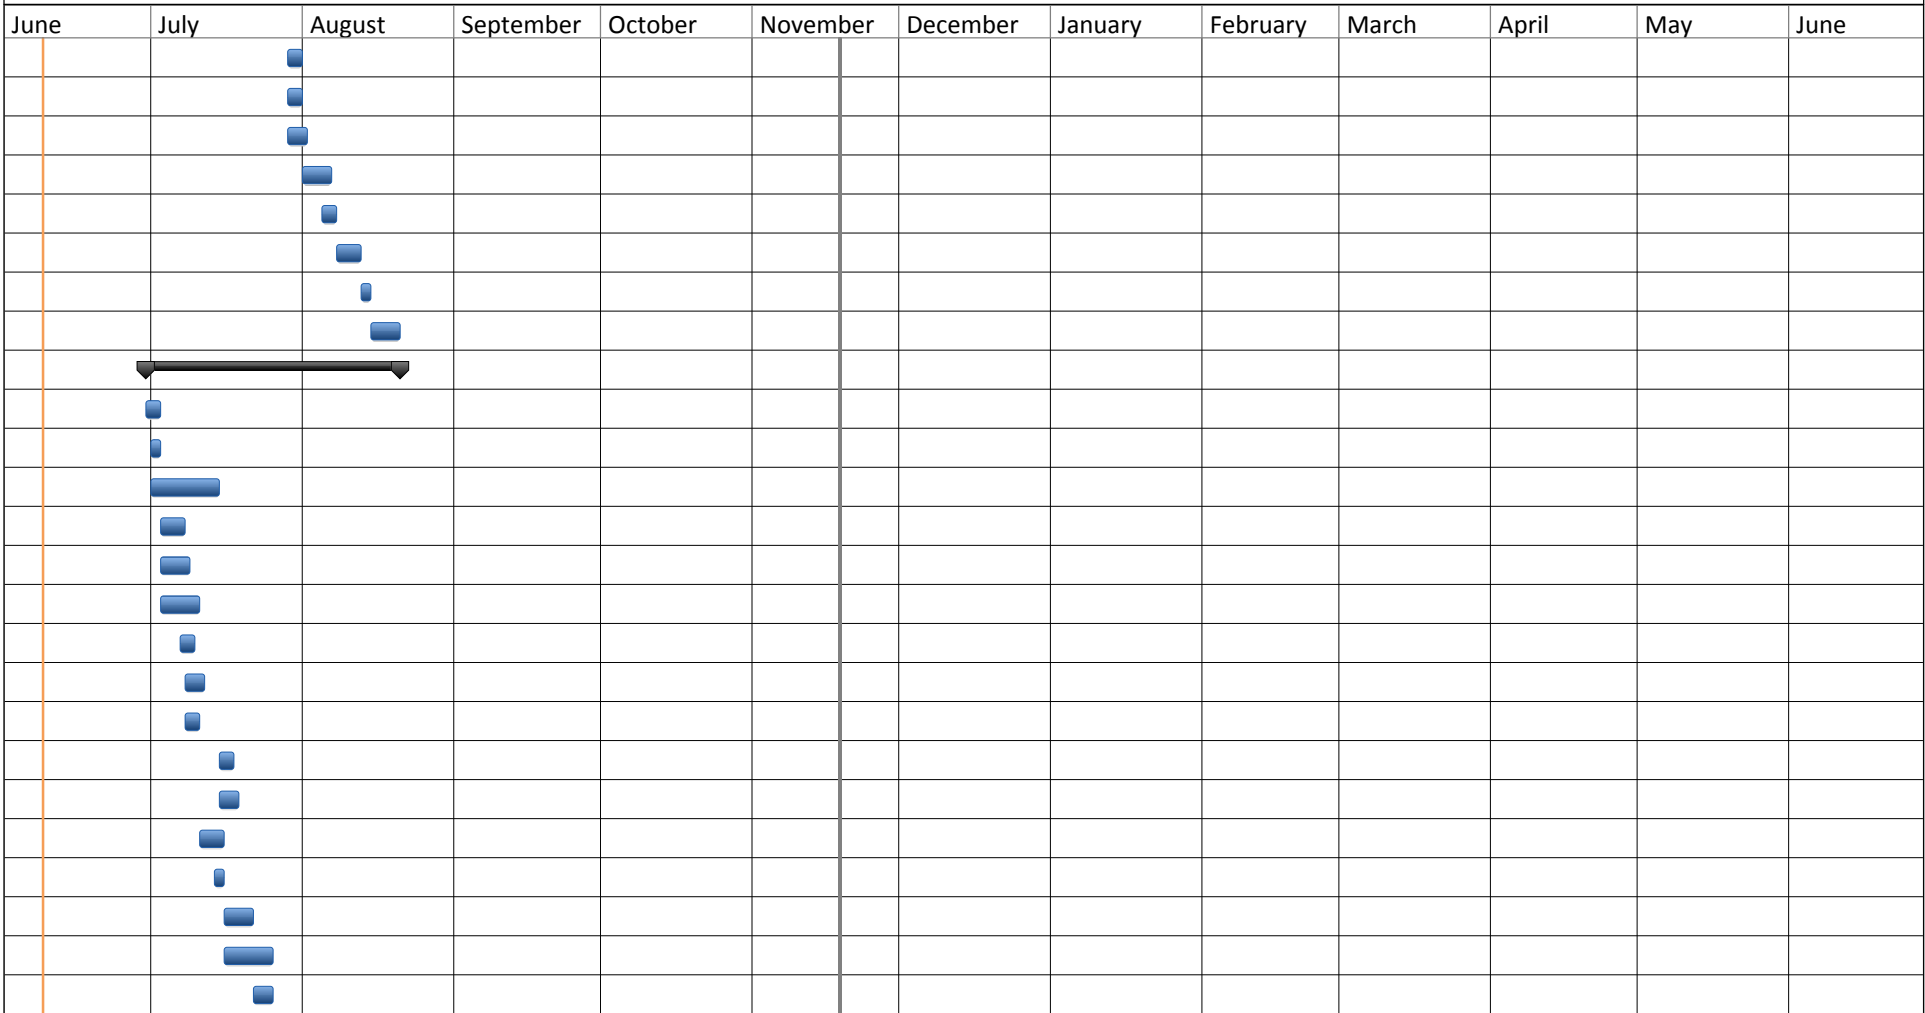

Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014



Finish Tue 11/18/14

Buford-Thompson Company

316 Granbury SV (6.9.14) SHB

Granbury ISD Renovations 2014

June	July	August	September	October	November	December	January	February	March	April	May	June
												
												
												
												
												
												
												
												
												
												
												
												
												
												
